



| ID |  | Task Mode                                                                           | Task Name                                                                              | Duration | Start        | Finish       | Predecessors | Resource Names | <div>18 Jul '22</div> <div>S M T W T F S S</div>                                    |  |  |  |  |  |  |  |  |  |  |  |  |  | 2 |
|----|----------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------|----------|--------------|--------------|--------------|----------------|-------------------------------------------------------------------------------------|--|--|--|--|--|--|--|--|--|--|--|--|--|---|
| 1  |                                                                                  |    | DataTrust Security Architecture Project                                                | 101 days | Mon 18/07/22 | Sun 4/12/22  |              |                |  |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 2  |                                                                                  |    | 1. Planning                                                                            | 10 days  | Mon 18/07/22 | Fri 29/07/22 |              |                |  |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 3  |                                                                                  |    | 1.1. Consulting stakeholder requirements and analyzing client's network infrastructure | 5 days   | Mon 18/07/22 | Fri 22/07/22 |              |                |  |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 4  |                                                                                  |    | 1.2. Discuss project requirements                                                      | 2 days   | Mon 18/07/22 | Tue 19/07/22 |              |                |  |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 5  |                                                                                  |    | 1.3. Assessing feasibility                                                             | 3 days   | Sat 23/07/22 | Tue 26/07/22 | 3            |                |  |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 6  |                                                                                  |    | 1.4. Risk assessment                                                                   | 2 days   | Wed 27/07/22 | Thu 28/07/22 | 5            |                |                                                                                     |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 7  |                                                                                  |    | 1.5. Creating project plan documentation                                               | 10 days  | Mon 18/07/22 | Fri 29/07/22 | 2            |                |  |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 8  |                                                                                  |    | 1.6. Project plan approval                                                             | 0 days   | Fri 29/07/22 | Fri 29/07/22 | 7            |                |                                                                                     |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 9  |                                                                                  |    | 2. Design                                                                              | 14 days  | Mon 1/08/22  | Thu 18/08/22 | 2            |                |                                                                                     |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 10 |                                                                                  |    | 2.1. Researching tools and technologies for security architecture                      | 5 days   | Mon 1/08/22  | Fri 5/08/22  |              |                |                                                                                     |  |  |  |  |  |  |  |  |  |  |  |  |  |   |
| 11 |                                                                                  |  | 2.2. Consulting stakeholders and client requirements                                   | 1 day    | Mon 1/08/22  | Mon 1/08/22  | 10           |                |                                                                                     |  |  |  |  |  |  |  |  |  |  |  |  |  |   |

Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID |  | Task Mode                                                                         | Task Name                                                                       | Duration | Start        | Finish       | Predecessors | Resource Names | S | 18 Jul '22 | M | T | W | T | F | S | S | 2 |
|----|----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|---------------------------------------------------------------------------------|----------|--------------|--------------|--------------|----------------|---|------------|---|---|---|---|---|---|---|---|
| 12 |                                                                                  |  | 2.3. Creating design for security architecture                                  | 5 days   | Mon 8/08/22  | Fri 12/08/22 | 10           |                |   |            |   |   |   |   |   |   |   |   |
| 13 |                                                                                  |  | 2.4. Review and approval of security architecture proposal                      | 1 day    | Sat 13/08/22 | Sat 13/08/22 | 12           |                |   |            |   |   |   |   |   |   |   |   |
| 14 |                                                                                  |  | 2.5. Create and finalize documentation for security architecture design         | 1 day    | Sun 14/08/22 | Sun 14/08/22 | 12           |                |   |            |   |   |   |   |   |   |   |   |
| 15 |                                                                                  |  | 2.6. Discussion and implementation of tools or methods of monitoring project    | 0 days   | Sun 14/08/22 | Sun 14/08/22 | 13           |                |   |            |   |   |   |   |   |   |   |   |
| 16 |                                                                                  |  | Contingencies                                                                   | 4 days   | Mon 15/08/22 | Thu 18/08/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 17 |                                                                                  |  | 3. Implementation                                                               | 49 days  | Fri 19/08/22 | Wed 26/10/22 | 9            |                |   |            |   |   |   |   |   |   |   |   |
| 18 |                                                                                  |  | 3.1. Obtaining all equipment, technology and software for security architecture | 14 days  | Fri 19/08/22 | Wed 7/09/22  |              |                |   |            |   |   |   |   |   |   |   |   |

Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |  Task Mode | Task Name                                                        | Duration | Start        | Finish       | Predecessors | Resource Names | S | 18 Jul '22 | M | T | W | T | F | S | S | 2 |
|----|--------------------------------------------------------------------------------------------|------------------------------------------------------------------|----------|--------------|--------------|--------------|----------------|---|------------|---|---|---|---|---|---|---|---|
| 19 |           | 3.2. Arranging security clearance and access to the server rooms | 7 days   | Fri 19/08/22 | Mon 29/08/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 20 |           | 3.3. Initiation and implementation of security architecture      | 21 days  | Thu 8/09/22  | Thu 6/10/22  | 18           |                |   |            |   |   |   |   |   |   |   |   |
| 21 |           | 3.4. Monitoring progress and development of architecture         | 49 days  | Fri 19/08/22 | Wed 26/10/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 22 |           | 3.5. Creation of implementation documentation and logs           | 7 days   | Fri 7/10/22  | Mon 17/10/22 | 20           |                |   |            |   |   |   |   |   |   |   |   |
| 23 |           | 3.6. Security architecture implementation approval               | 0 days   | Mon 17/10/22 | Mon 17/10/22 | 22           |                |   |            |   |   |   |   |   |   |   |   |
| 24 |           | Contingencies                                                    | 7 days   | Tue 18/10/22 | Wed 26/10/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 25 |           | 4. Evaluation                                                    | 7 days   | Thu 27/10/22 | Fri 4/11/22  | 17           |                |   |            |   |   |   |   |   |   |   |   |
| 26 |           | 4.1. Functionality testing of security architecture              | 2 days   | Thu 27/10/22 | Fri 28/10/22 |              |                |   |            |   |   |   |   |   |   |   |   |

Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID |  | Task Mode                                                                         | Task Name                                                                                 | Duration | Start        | Finish       | Predecessors | Resource Names | S | 18 Jul '22 | M | T | W | T | F | S | S | 2 |
|----|----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------|----------|--------------|--------------|--------------|----------------|---|------------|---|---|---|---|---|---|---|---|
| 27 |                                                                                  |  | 4.2. Penetration testing and vulnerability scans of network infrastructure                | 2 days   | Thu 27/10/22 | Fri 28/10/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 28 |                                                                                  |  | 4.3. Documentation of all tests and identified vulnerabilities including logs and reports | 4 days   | Thu 27/10/22 | Tue 1/11/22  |              |                |   |            |   |   |   |   |   |   |   |   |
| 29 |                                                                                  |  | 4.4. Evaluation and documentation review, analysis and approval                           | 1 day    | Wed 2/11/22  | Wed 2/11/22  | 28           |                |   |            |   |   |   |   |   |   |   |   |
| 30 |                                                                                  |  | Contingencies                                                                             | 2 days   | Thu 3/11/22  | Fri 4/11/22  |              |                |   |            |   |   |   |   |   |   |   |   |
| 31 |                                                                                  |  | 5. Hardening                                                                              | 8 days   | Sat 5/11/22  | Tue 15/11/22 | 25           |                |   |            |   |   |   |   |   |   |   |   |
| 32 |                                                                                  |  | 5.1. Elimination or mitigation of vulnerabilities including system optimization           | 3 days   | Sat 5/11/22  | Tue 8/11/22  |              |                |   |            |   |   |   |   |   |   |   |   |
| 33 |                                                                                  |  | 5.2. Penetration tests and vulnerability scans                                            | 3 days   | Sat 5/11/22  | Tue 8/11/22  | 32           |                |   |            |   |   |   |   |   |   |   |   |

Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |  | Task Mode                                                                         | Task Name                                                             | Duration | Start        | Finish       | Predecessors | Resource Names | S | 18 Jul '22 | M | T | W | T | F | S | S | 2 |
|----|----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-----------------------------------------------------------------------|----------|--------------|--------------|--------------|----------------|---|------------|---|---|---|---|---|---|---|---|
| 34 |                                                                                  |  | 5.3. Documentation of pen test results and analysis                   | 2 days   | Wed 9/11/22  | Thu 10/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 35 |                                                                                  |  | 5.4. Analysis, review and approval of security architecture           | 3 days   | Wed 9/11/22  | Fri 11/11/22 | 34           |                |   |            |   |   |   |   |   |   |   |   |
| 36 |                                                                                  |  | Contingencies                                                         | 3 days   | Sat 12/11/22 | Tue 15/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 37 |                                                                                  |  | 6. Documentation                                                      | 5 days   | Wed 16/11/22 | Tue 22/11/22 | 31           |                |   |            |   |   |   |   |   |   |   |   |
| 38 |                                                                                  |  | 6.1. Creation of support documentation for client                     | 3 days   | Wed 16/11/22 | Fri 18/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 39 |                                                                                  |  | 6.2. Creation of backup and disaster recovery procedure documentation | 3 days   | Wed 16/11/22 | Fri 18/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 40 |                                                                                  |  | 6.3. Analysis and review of all created documentation                 | 1 day    | Sat 19/11/22 | Sat 19/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 41 |                                                                                  |  | 6.4. Approval of all documentation                                    | 1 day    | Sun 20/11/22 | Sun 20/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 42 |                                                                                  |  | Contingencies                                                         | 2 days   | Mon 21/11/22 | Tue 22/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 43 |                                                                                  |  | 7. Closure                                                            | 2 days   | Wed 23/11/22 | Thu 24/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |


Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID |  | Task Mode                                                                         | Task Name                                                         | Duration | Start        | Finish       | Predecessors | Resource Names | S | 18 Jul '22 | M | T | W | T | F | S | S | 2 |
|----|----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------|----------|--------------|--------------|--------------|----------------|---|------------|---|---|---|---|---|---|---|---|
| 44 |                                                                                  |  | 7.1. Meeting and evaluation of project success and failures       | 1 day    | Wed 23/11/22 | Wed 23/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 45 |                                                                                  |  | 7.2. Completion of any unfinished tasks or application of changes | 2 days   | Wed 23/11/22 | Thu 24/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 46 |                                                                                  |  | 7.3. Sign off and handover                                        | 1 day    | Fri 25/11/22 | Fri 25/11/22 |              |                |   |            |   |   |   |   |   |   |   |   |
| 47 |                                                                                  |  | Contingencies                                                     | 7 days   | Sat 26/11/22 | Sun 4/12/22  |              |                |   |            |   |   |   |   |   |   |   |   |

Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22


|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

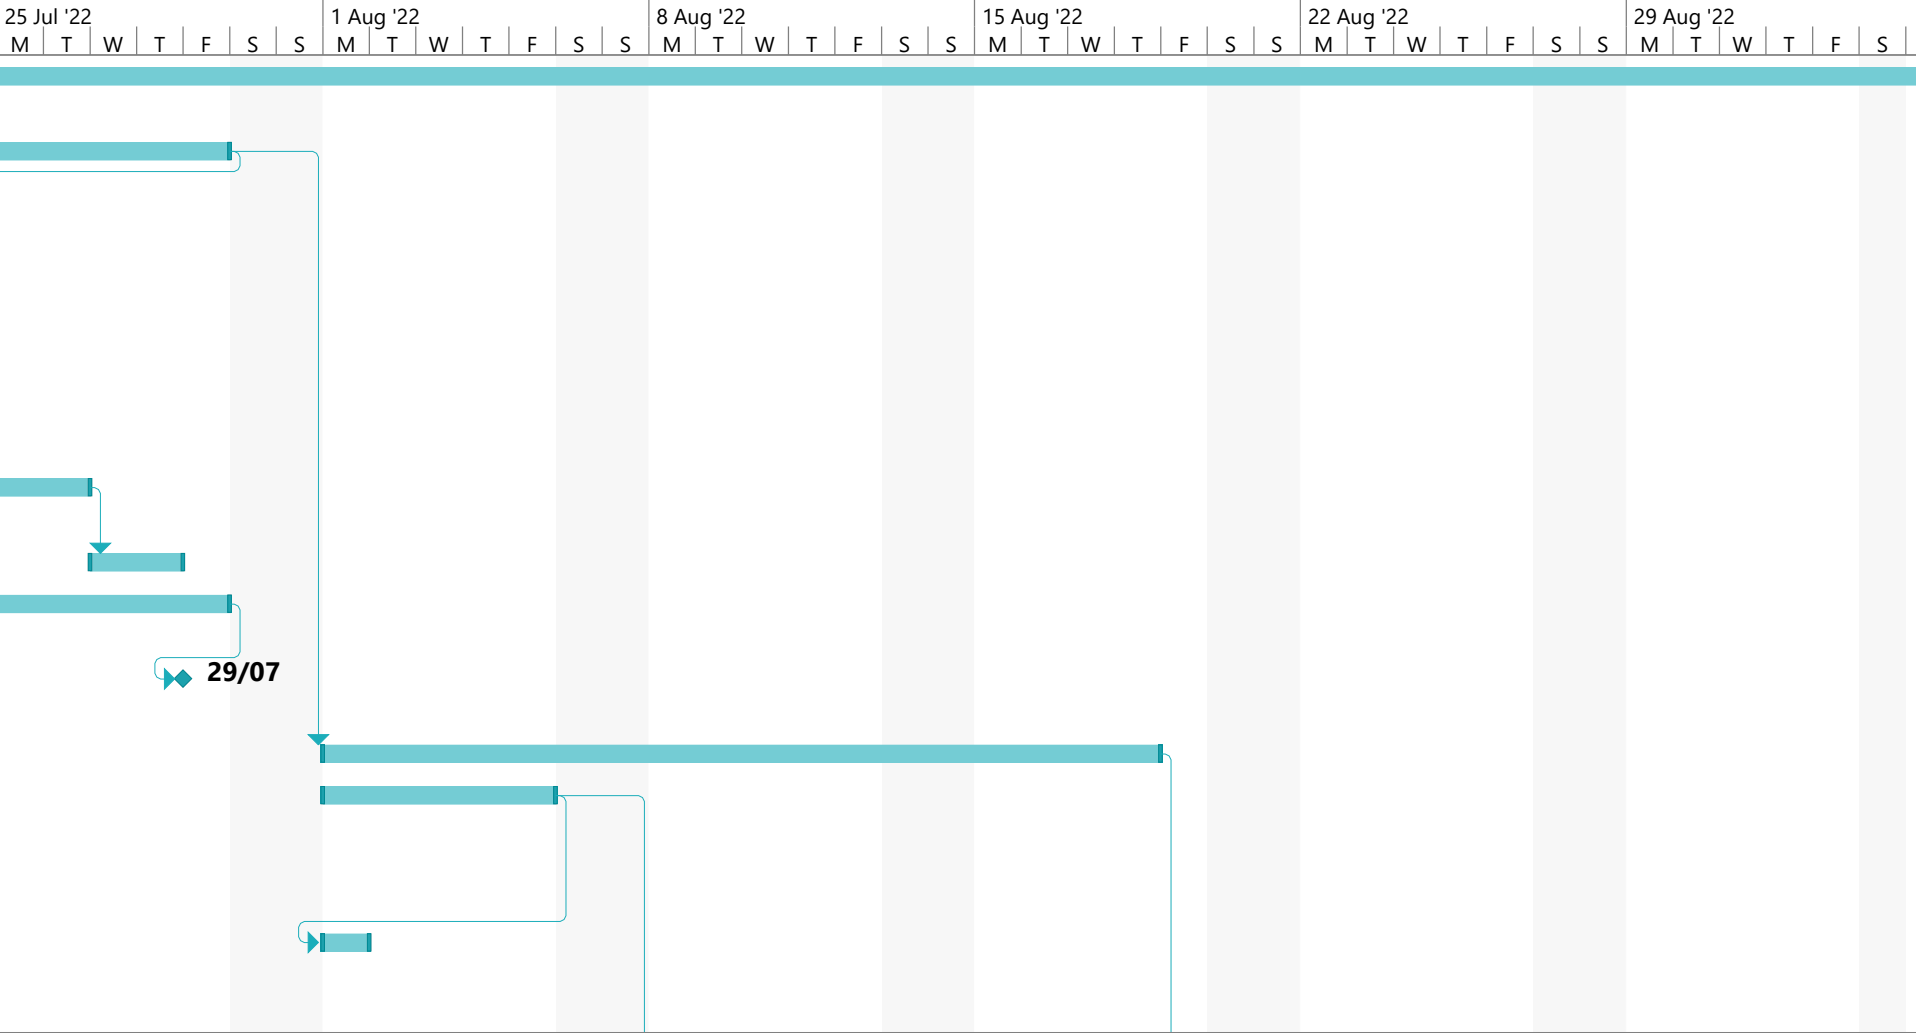

|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

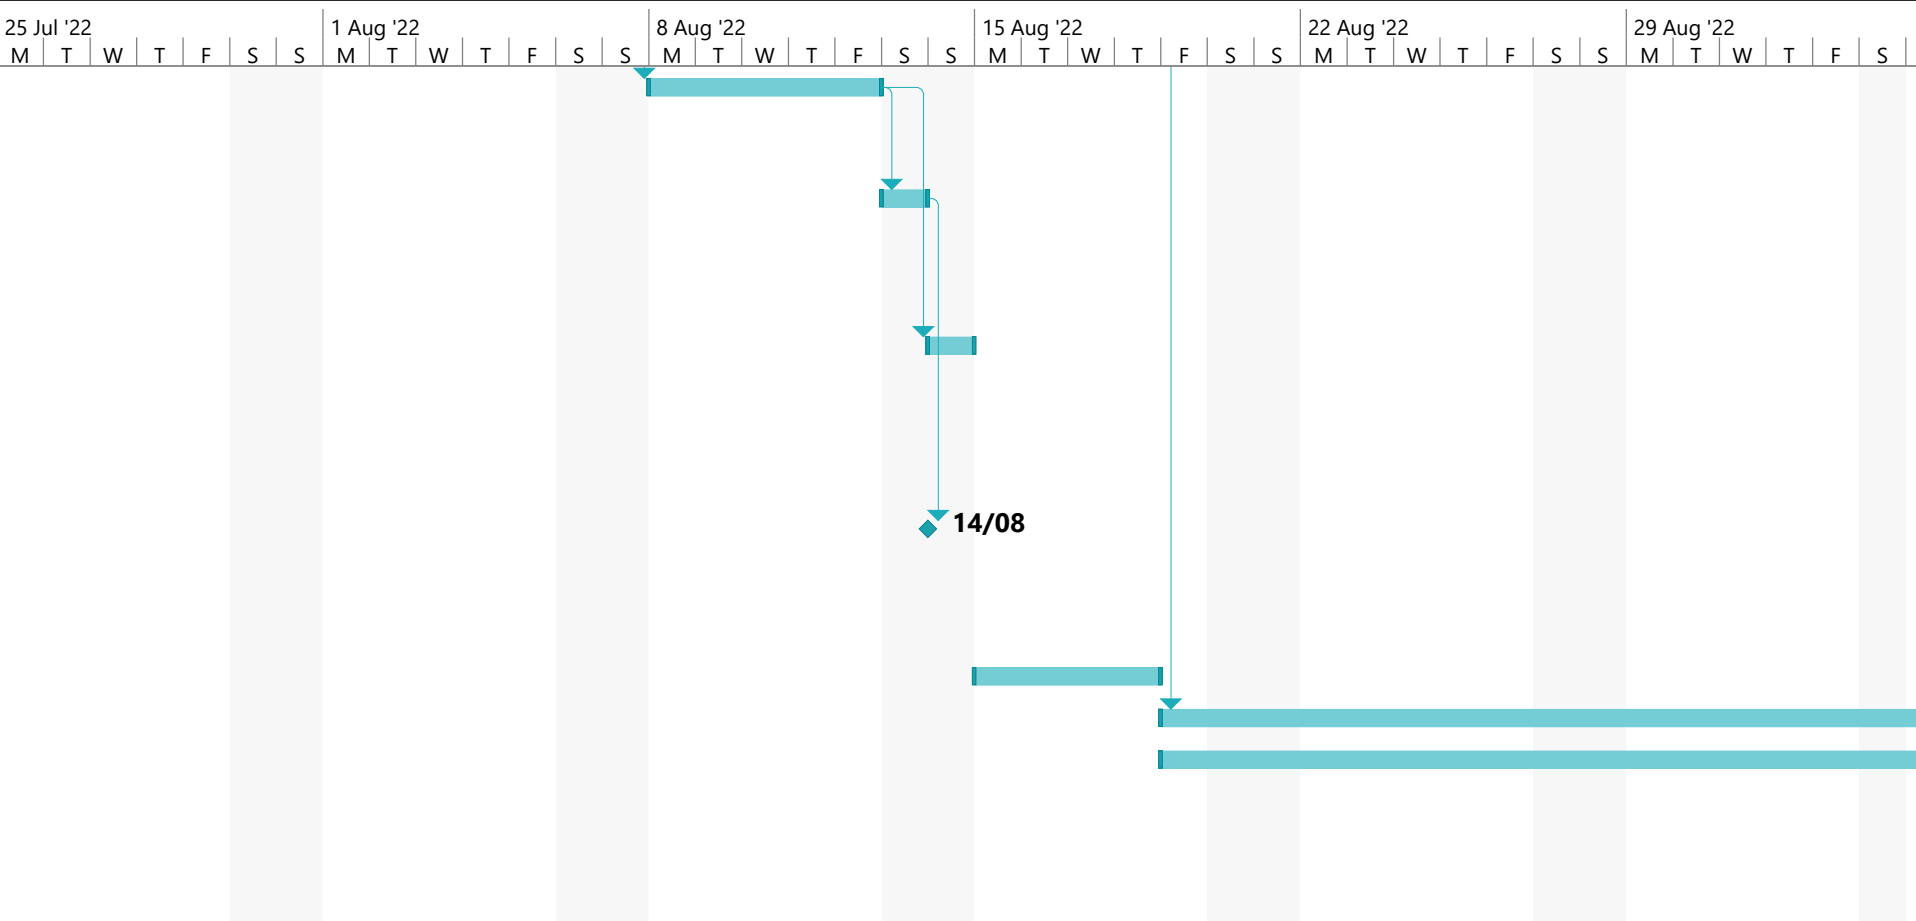

|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

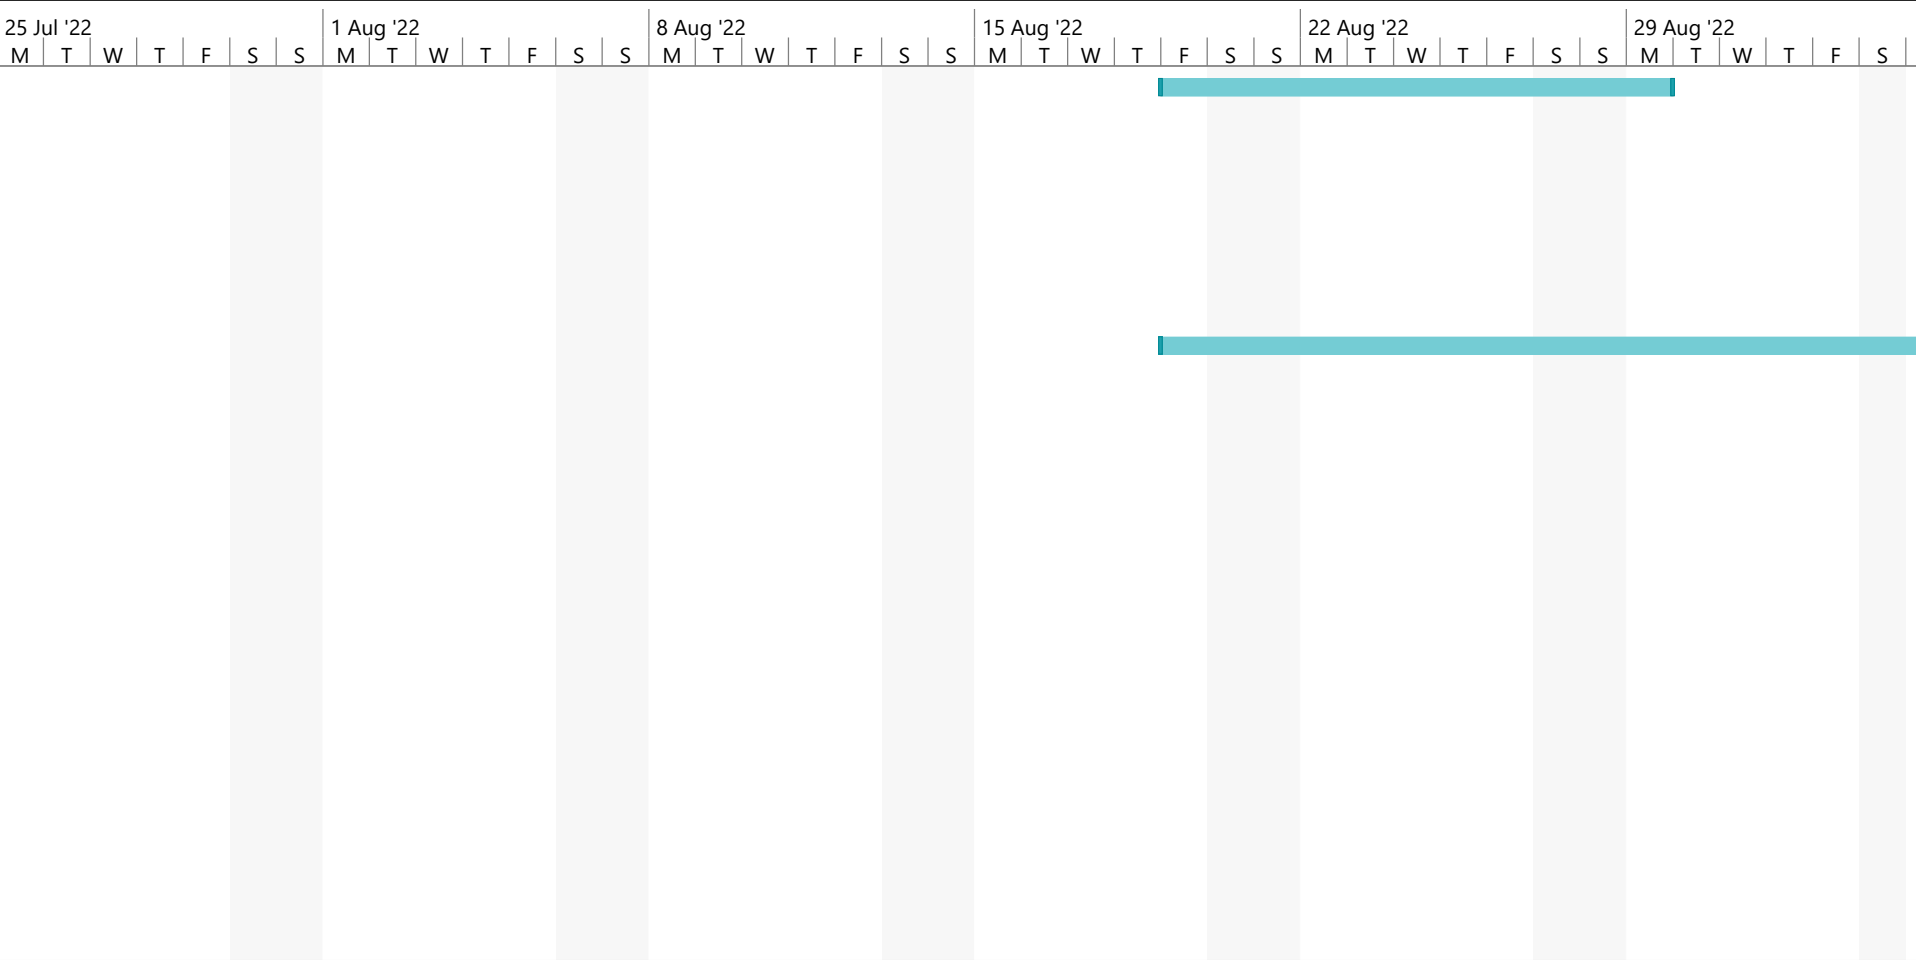


|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |





Project: Marco\_Cyb\_Sec\_Proj\_W


Date: Sat 26/11/22

|                    |             |                       |             |                    |             |
|--------------------|-------------|-----------------------|-------------|--------------------|-------------|
| Task               | <div></div> | Inactive Summary      | <div></div> | External Tasks     | <div></div> |
| Split              | <div></div> | Manual Task           | <div></div> | External Milestone | <div></div> |
| Milestone          | <div></div> | Duration-only         | <div></div> | Deadline           | <div></div> |
| Summary            | <div></div> | Manual Summary Rollup | <div></div> | Progress           | <div></div> |
| Project Summary    | <div></div> | Manual Summary        | <div></div> | Manual Progress    | <div></div> |
| Inactive Task      | <div></div> | Start-only            | <div></div> |                    |             |
| Inactive Milestone | <div></div> | Finish-only           | <div></div> |                    |             |




|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |




|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |



|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

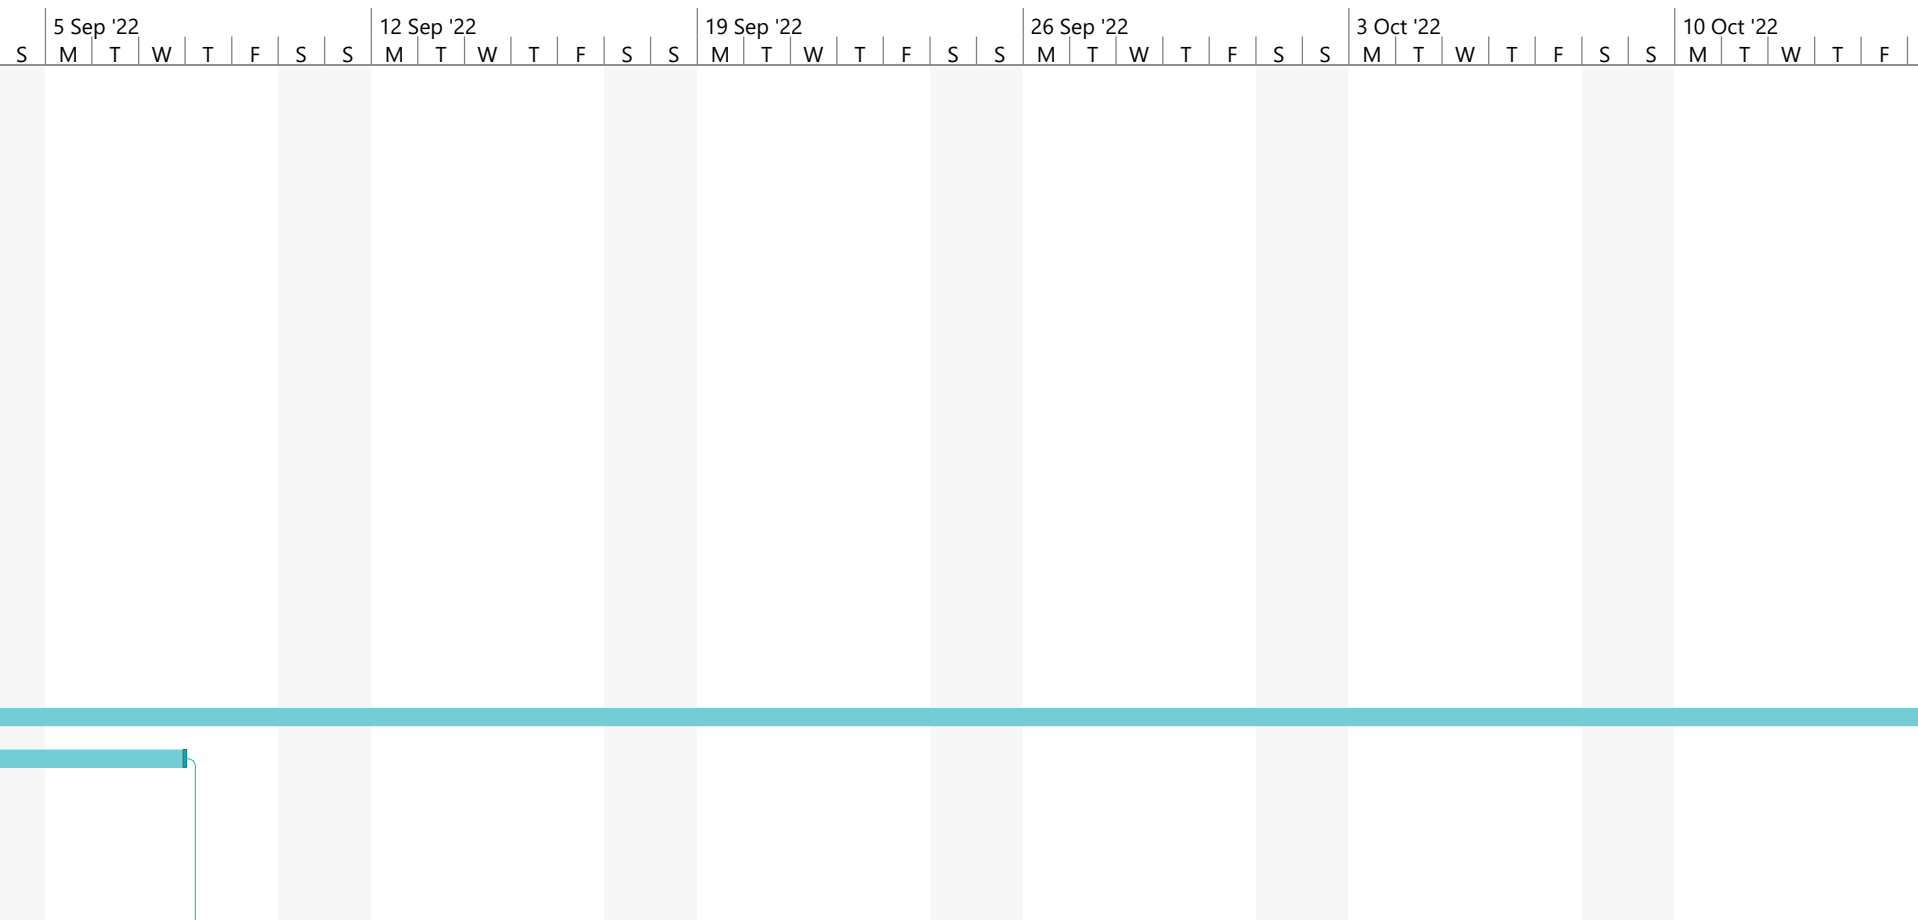


|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

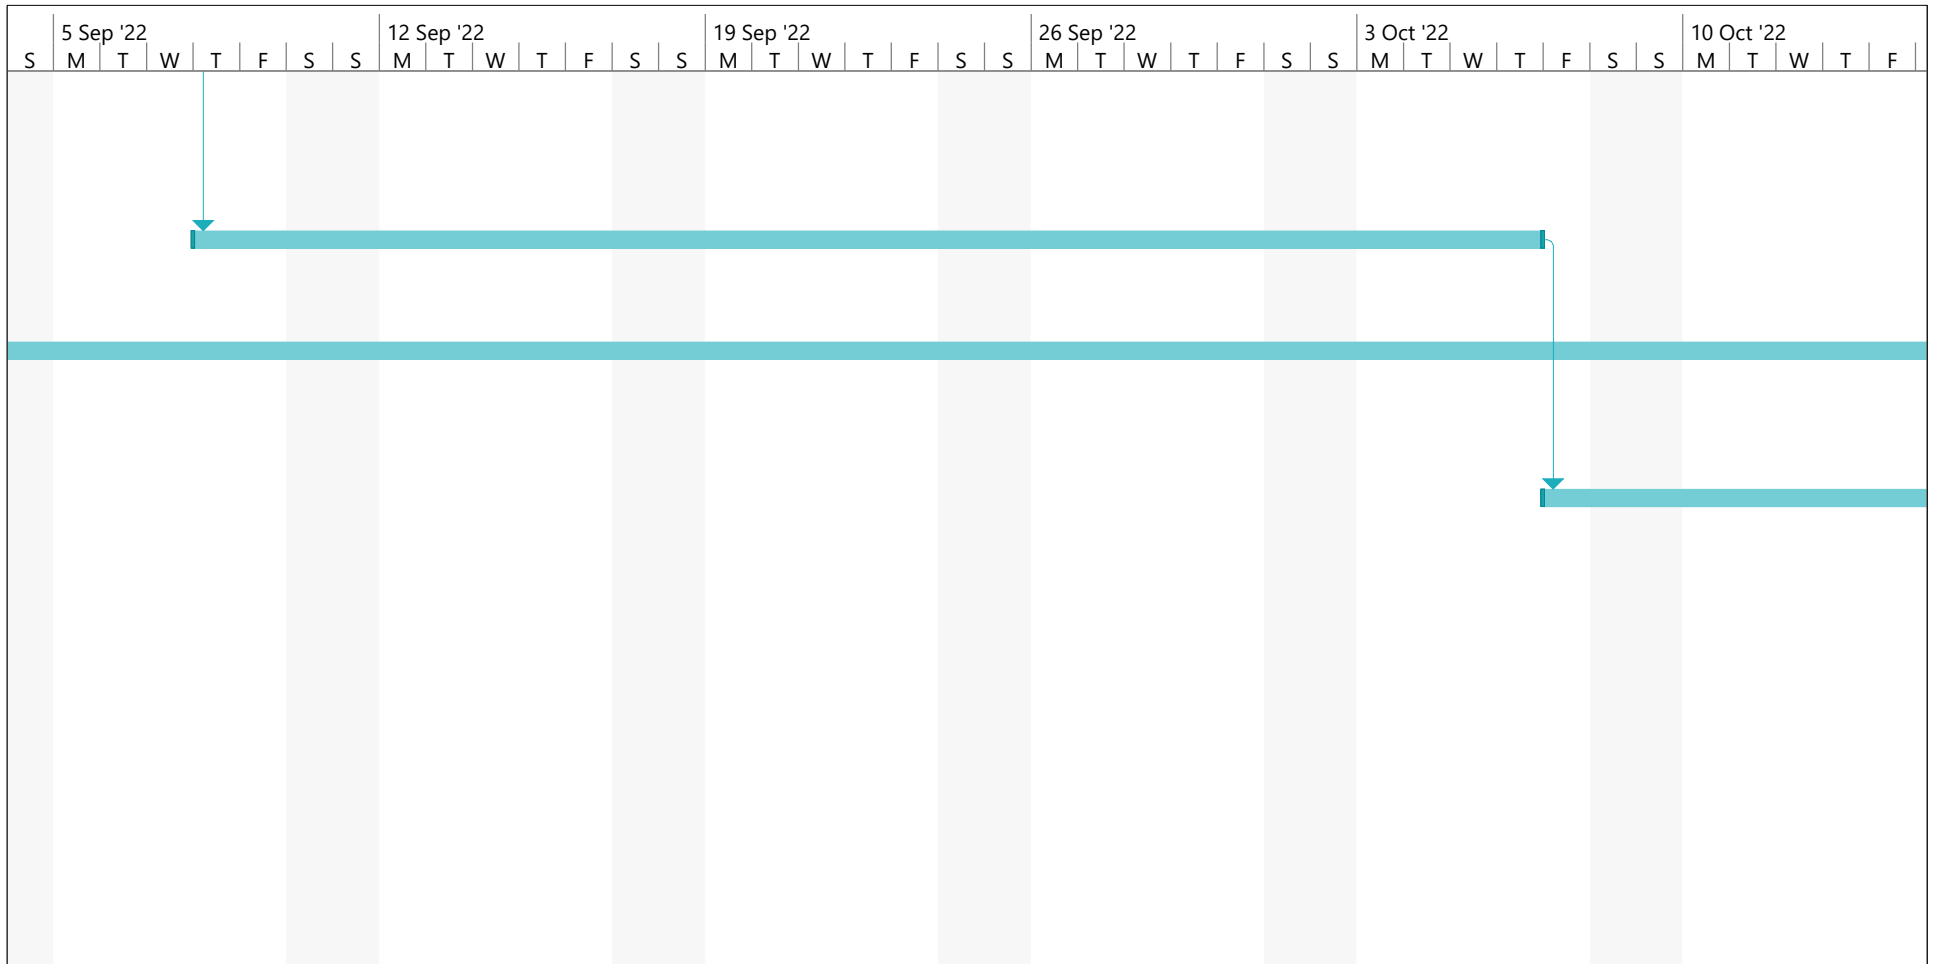


Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22


|                    |  |                       |  |                    |  |
|--------------------|--|-----------------------|--|--------------------|--|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |  |
| Inactive Milestone |  | Finish-only           |  |                    |  |





Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22


|                    |  |                       |  |                    |  |
|--------------------|--|-----------------------|--|--------------------|--|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |  |
| Inactive Milestone |  | Finish-only           |  |                    |  |

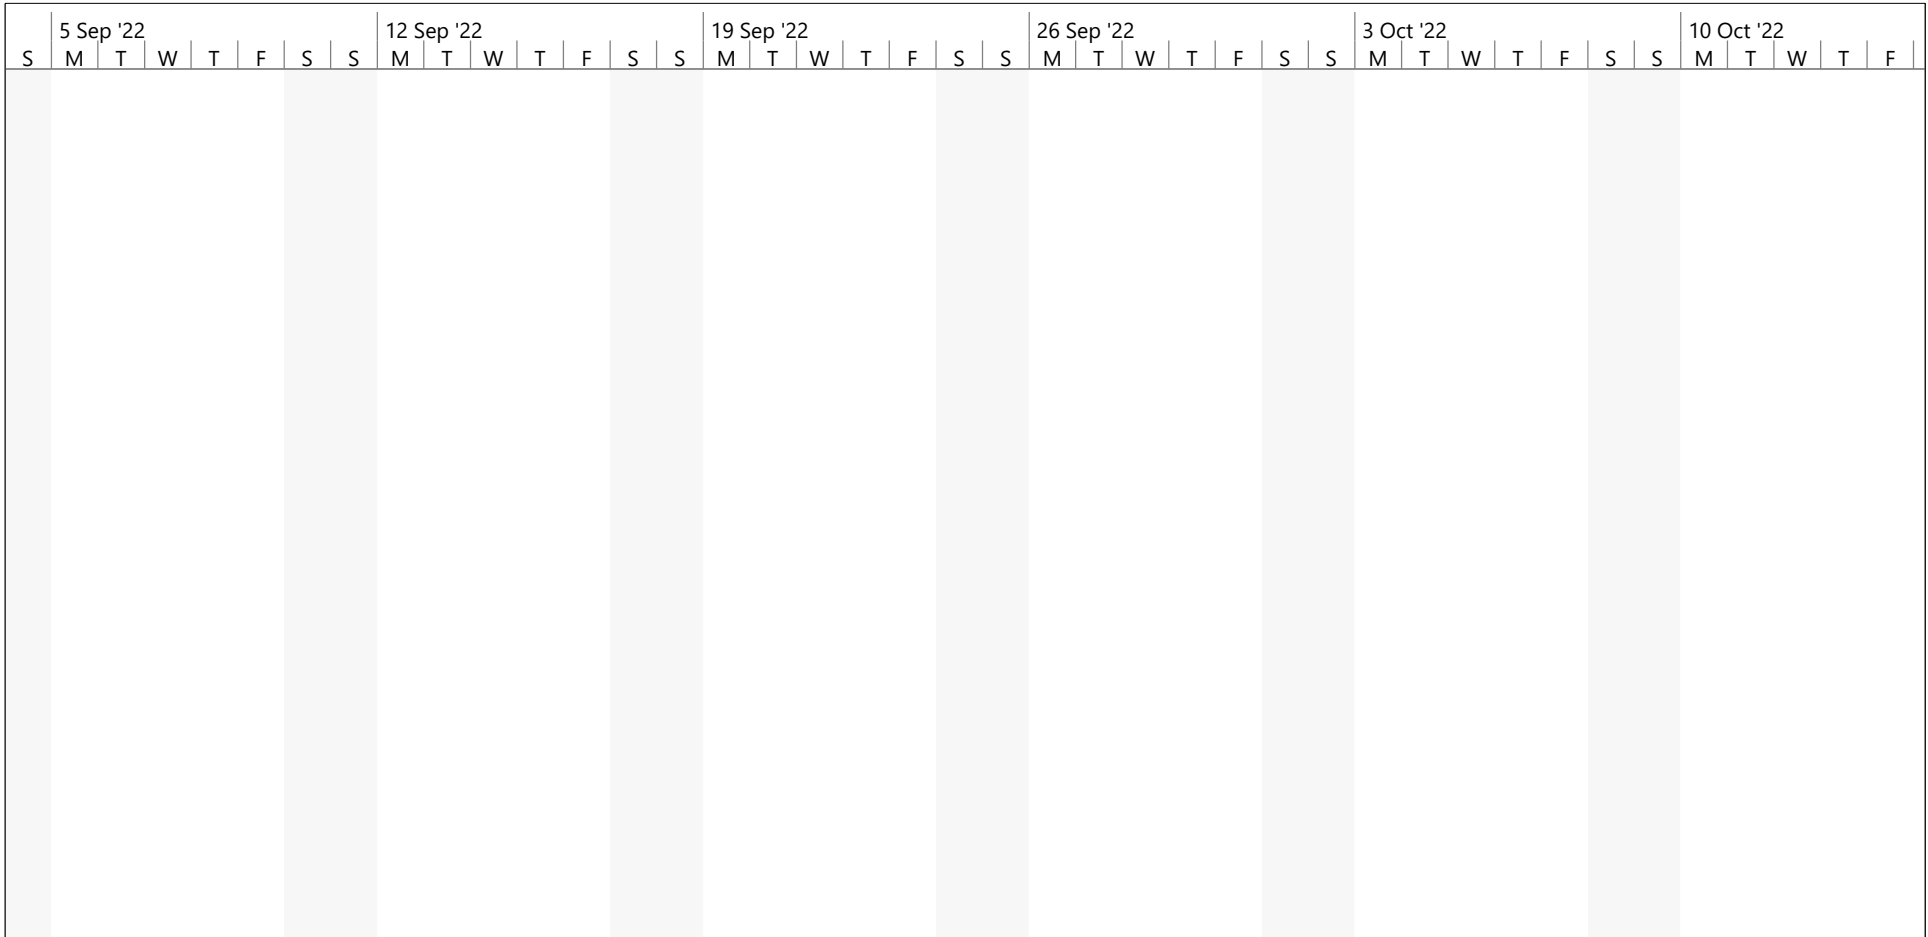


|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

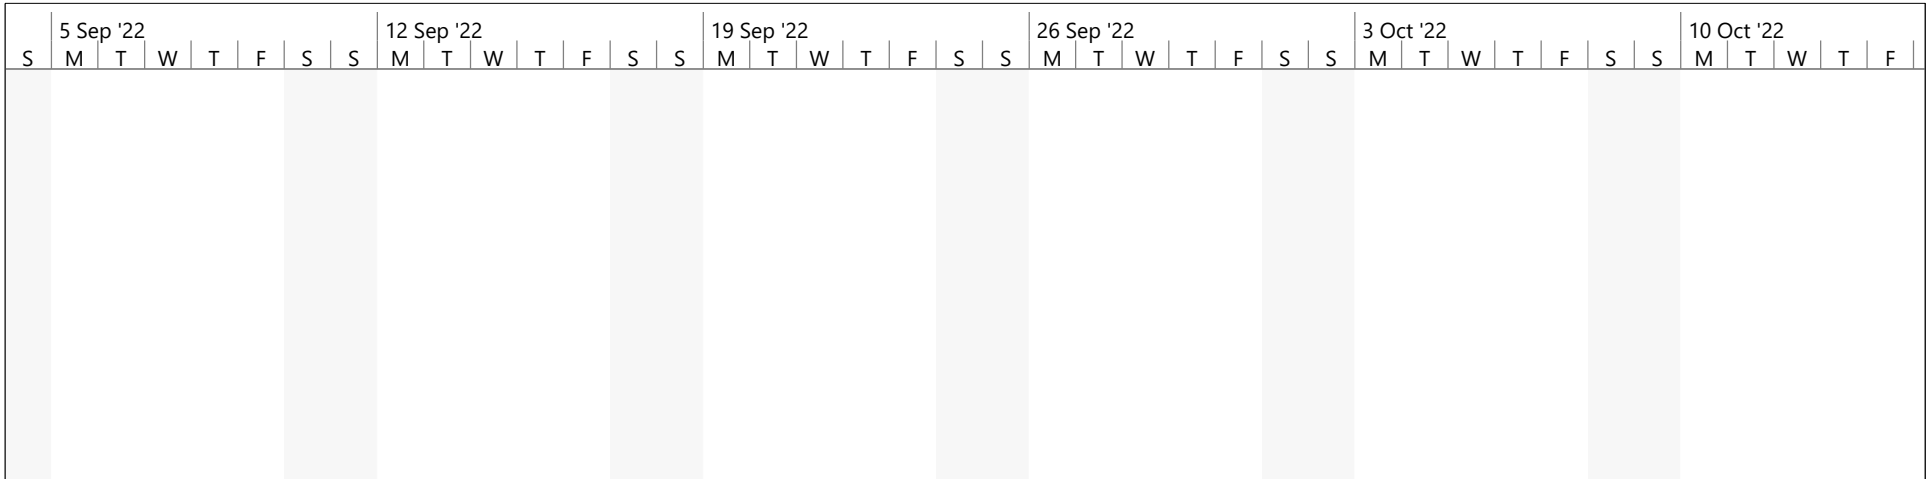


|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |



|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

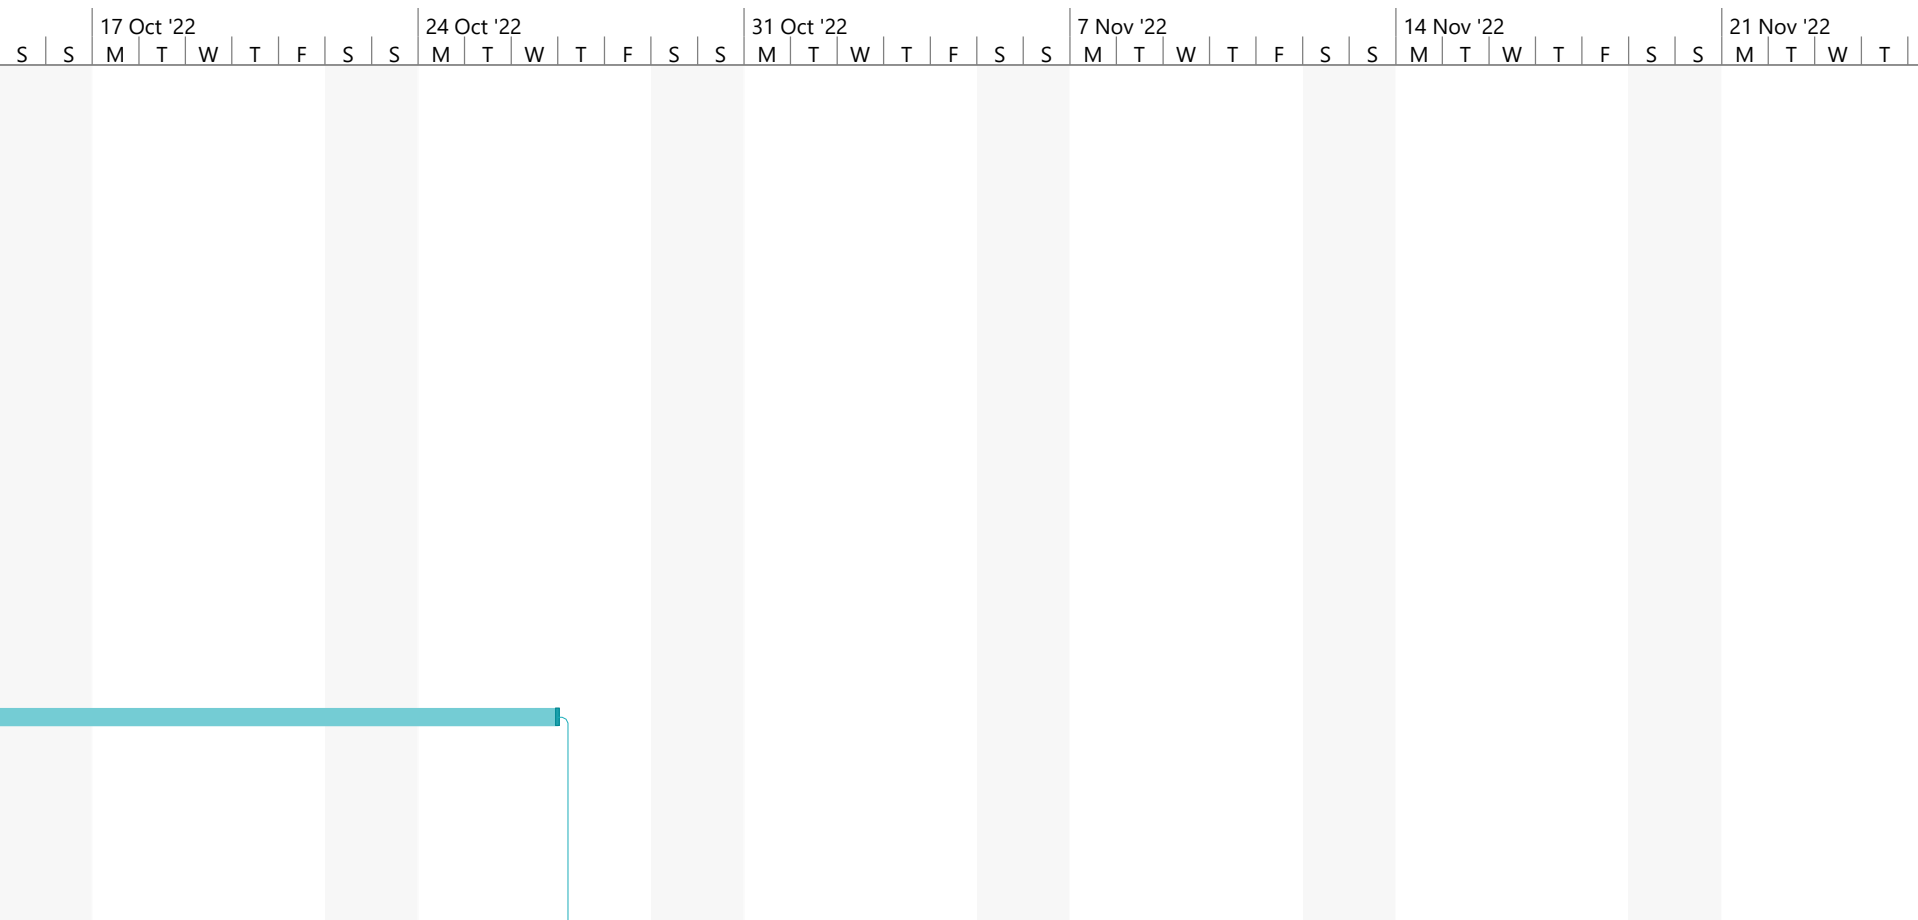


|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

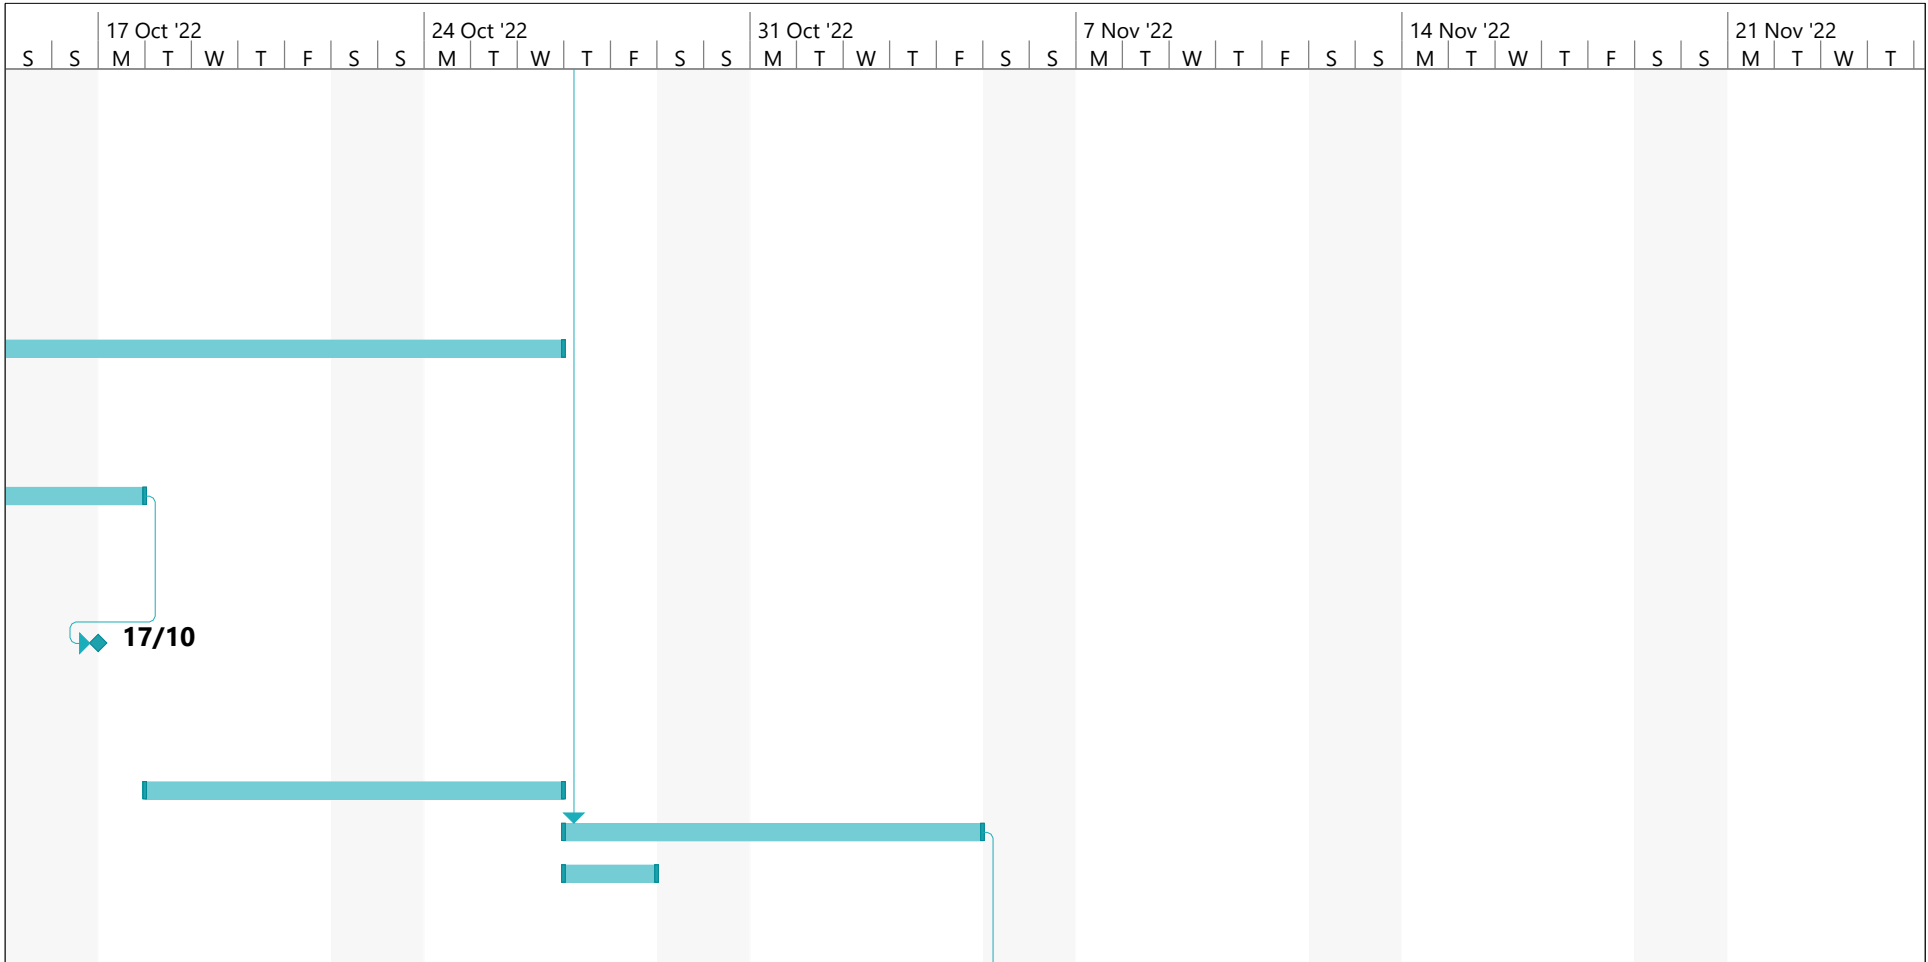

Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22


|                    |  |                       |  |                    |  |
|--------------------|--|-----------------------|--|--------------------|--|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |  |
| Inactive Milestone |  | Finish-only           |  |                    |  |




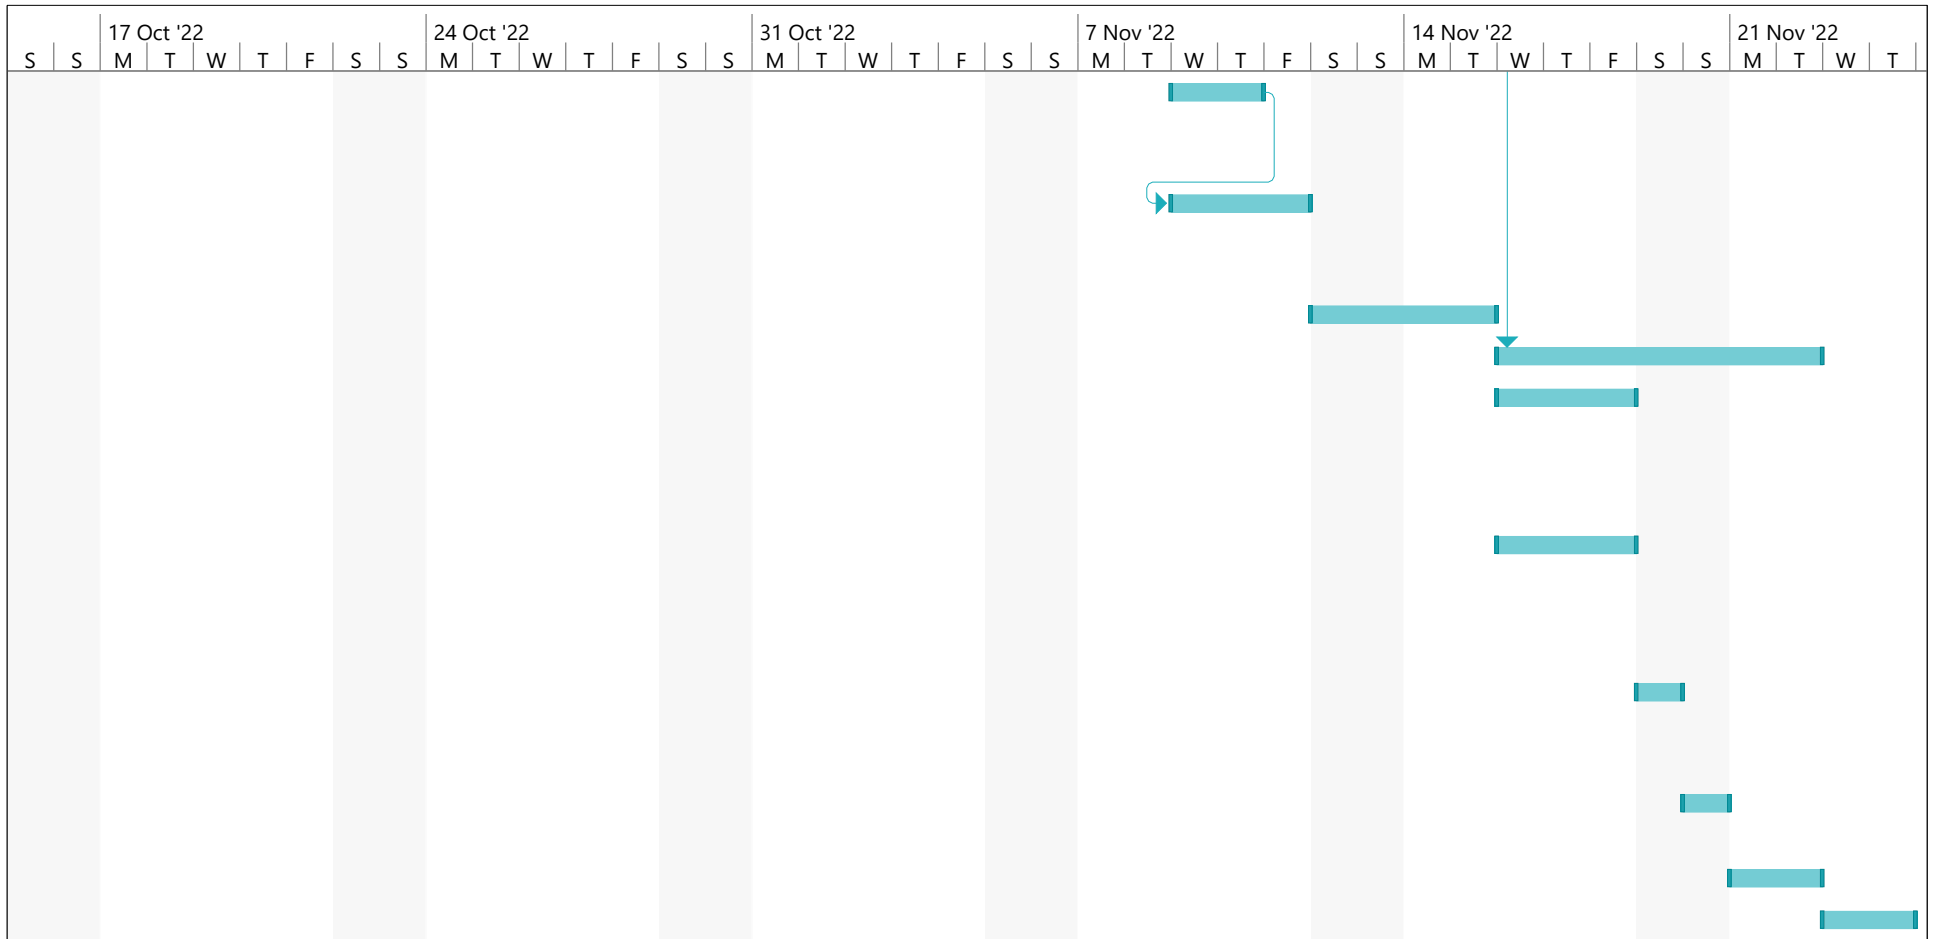


|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |







|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |




|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |





Project: Marco\_Cyb\_Sec\_Proj\_W  
Date: Sat 26/11/22


|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |





|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

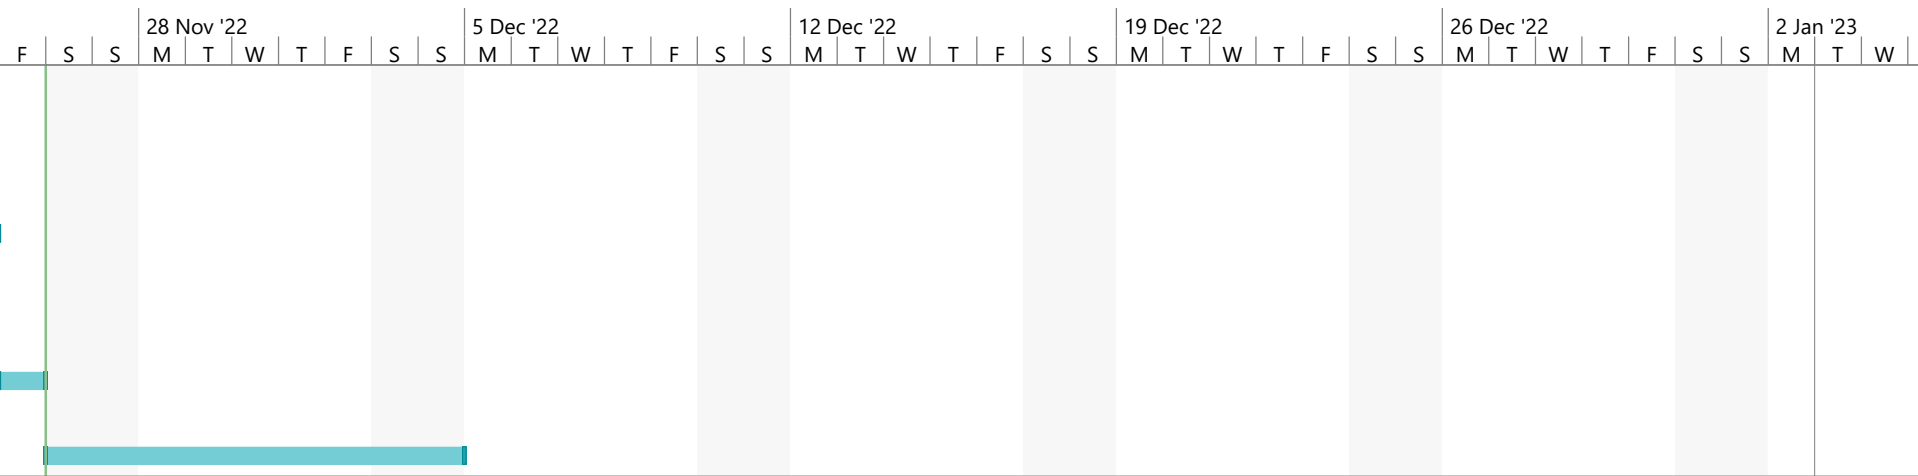

|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Marco_Cyb_Sec_Proj_W<br>Date: Sat 26/11/22 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |
